

Nibrexo OS AI

Development Roadmap v1.1 — Build Flows & Flowcharts

Editable source-style documentation for direct project editing and developer/AI-agent handoff.


Document status: Working blueprint | **Owner:** Nibrexo | **Use:** LLM Arena agent + development planning

How to use this document

- Is PDF ko master roadmap ki tarah use karein. Kisi phase, feature ya flow mein change ho to isi document ke next version mein update karein.
- Coding agent ko poora product ek single prompt mein dene ke bajaye phase-by-phase instructions dein.
- Har completed phase ko GitHub commit/tag ke saath freeze karein.
- Platform APIs ki actual capabilities ko implementation se pehle verify karein; unsupported features assume na karein.


1. Overall System Build Flow

High-level system ka basic flow:

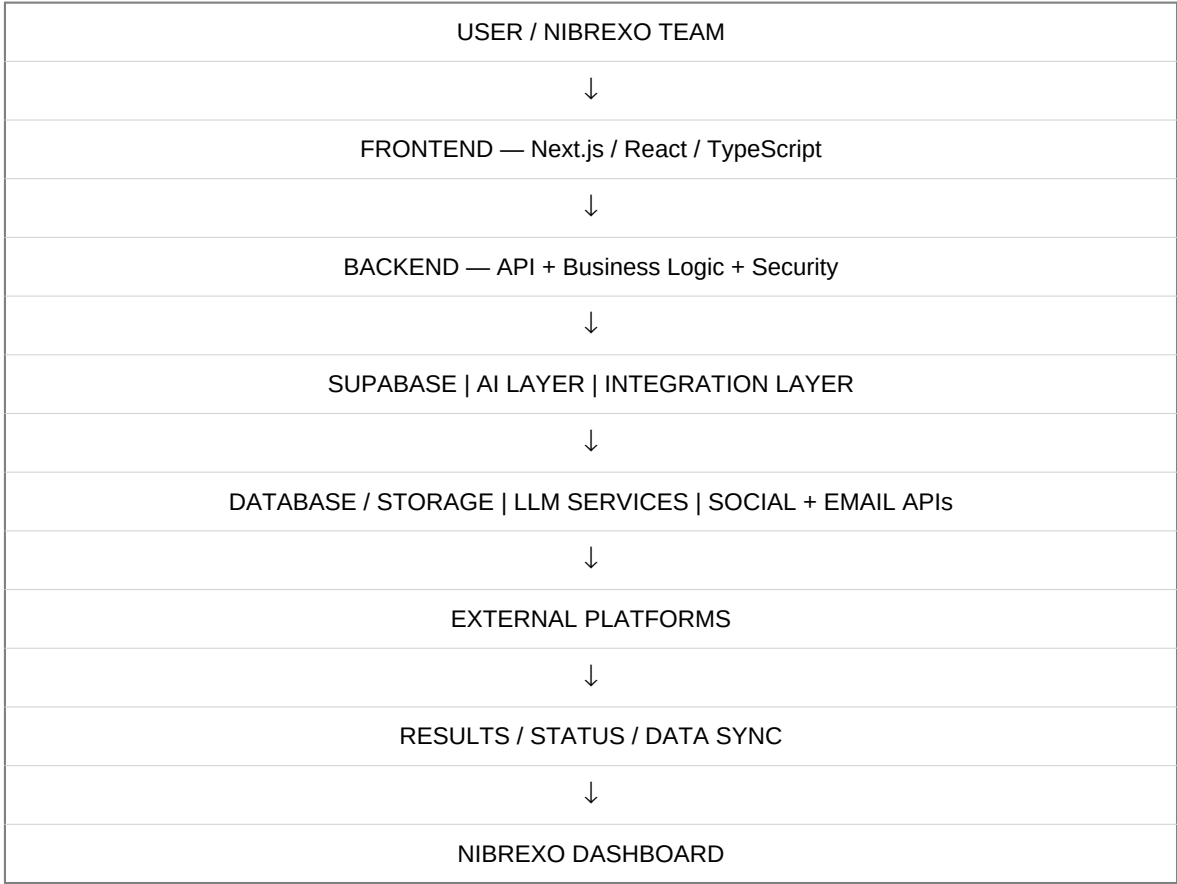


Core rule: frontend direct sensitive provider APIs ko control nahi karega. Sensitive credentials aur privileged operations backend/server-side layer ke through handle honge.


2. Complete MVP Build Map

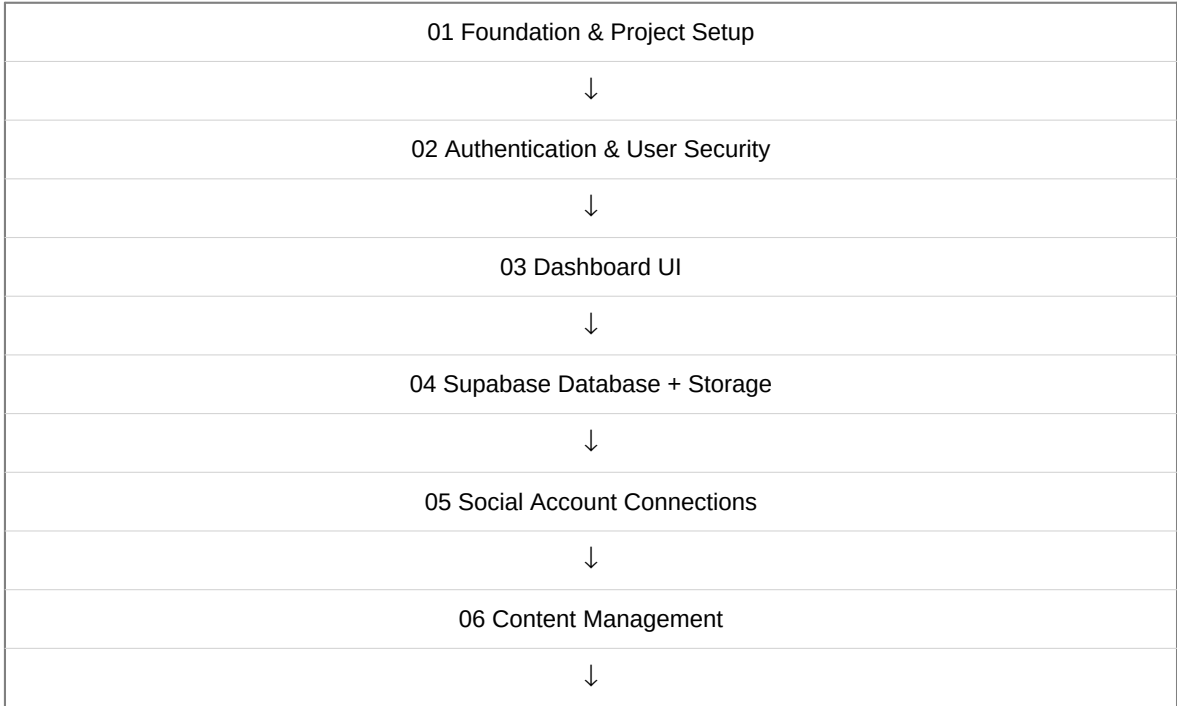




3. GitHub → Vercel Deployment Flow

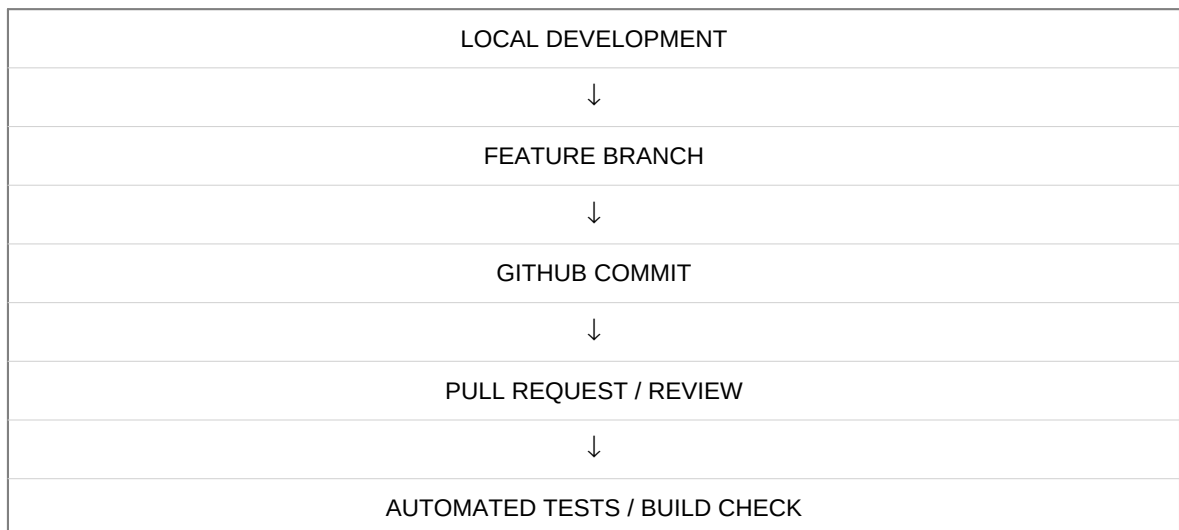

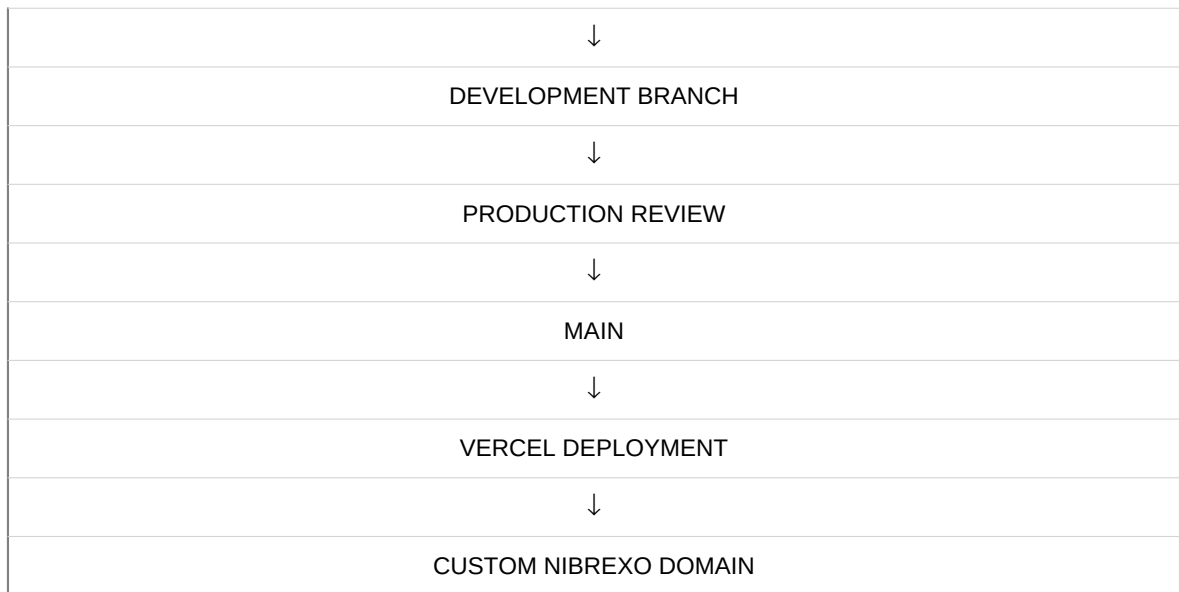

Environment separation: development/staging aur production ke secrets aur configurations separate rakhe jayenge.


4. Social Account Connection Flow

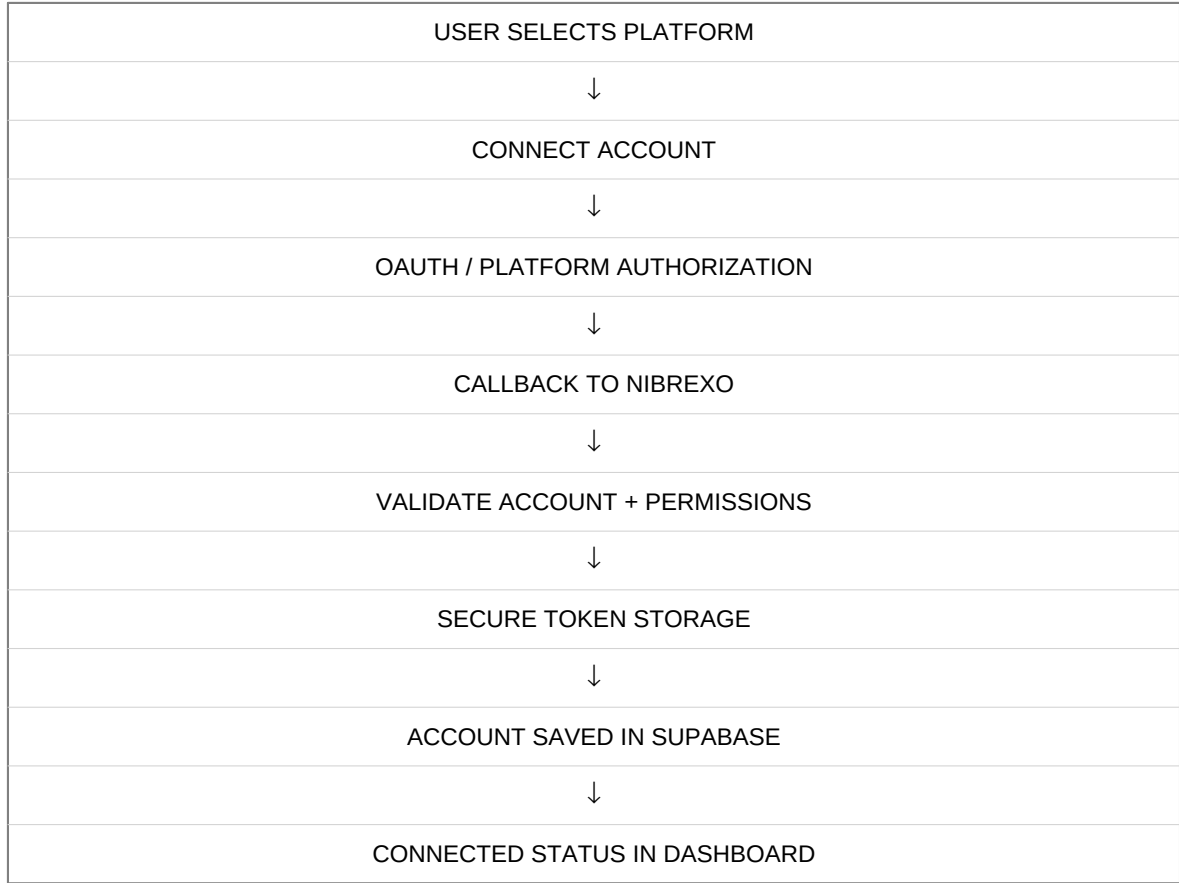


Platform adapter pattern:


Nibrexo Integration Layer Common interface Auth state Publishing state Error normalization	Platform Adapters YouTube Meta / Instagram / Facebook TikTok LinkedIn Pinterest
---	---

5. Content Upload & Publishing Flow

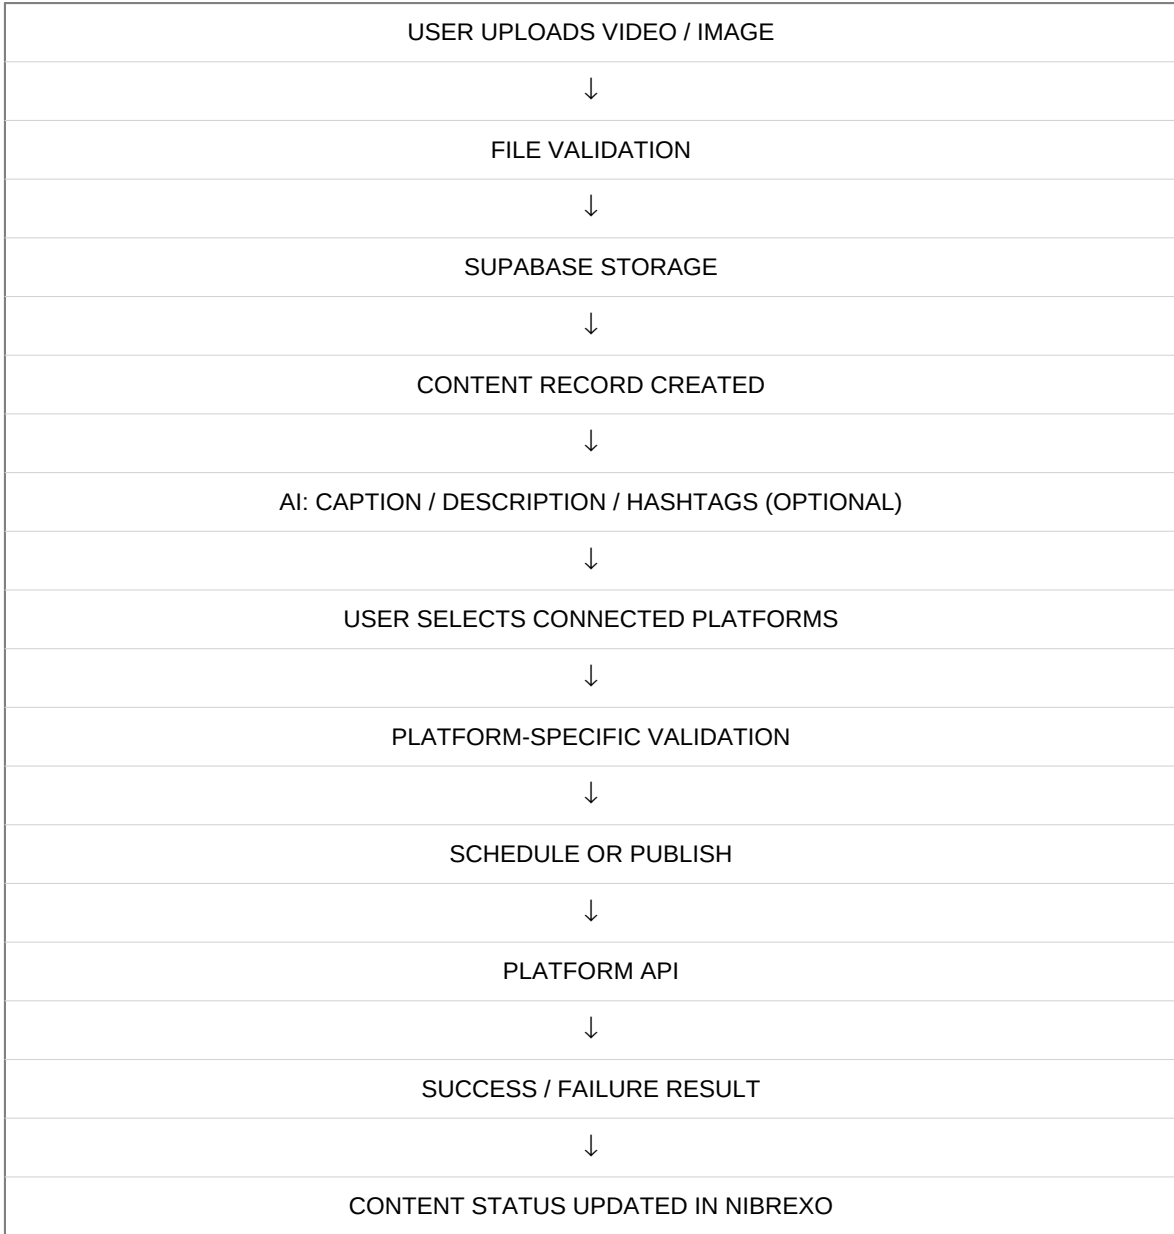


6. Unified Inbox Flow



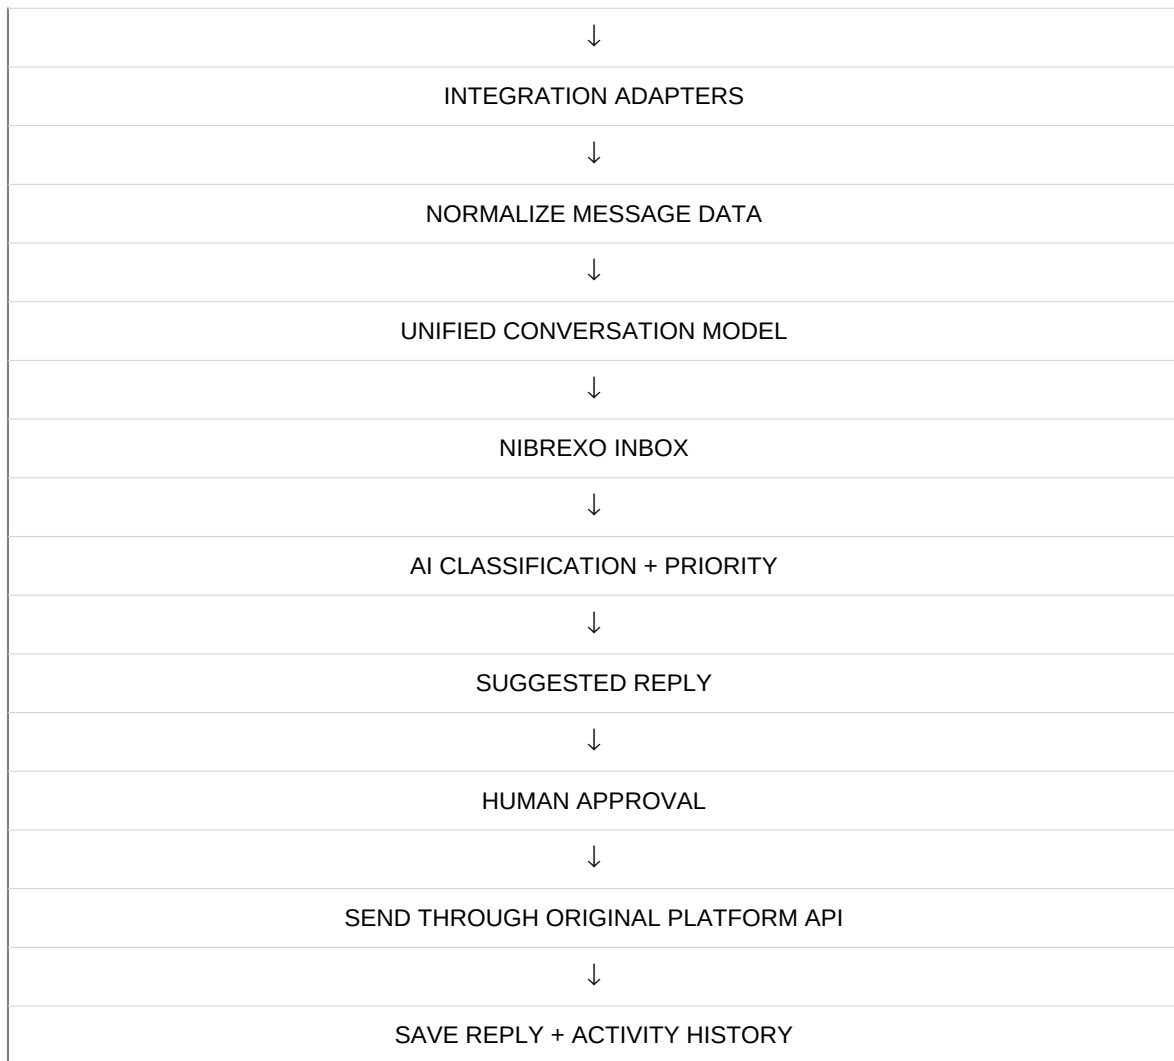


7. Email Automation Flow

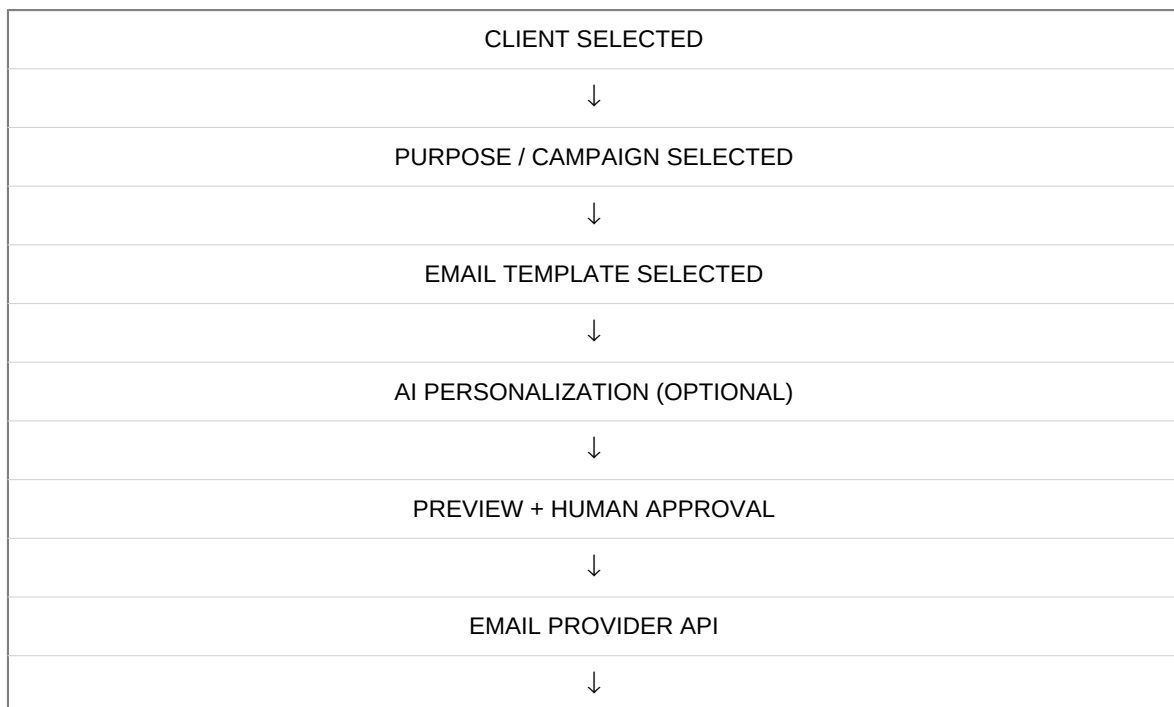



8. Nibrexo AI Agent Execution Flow

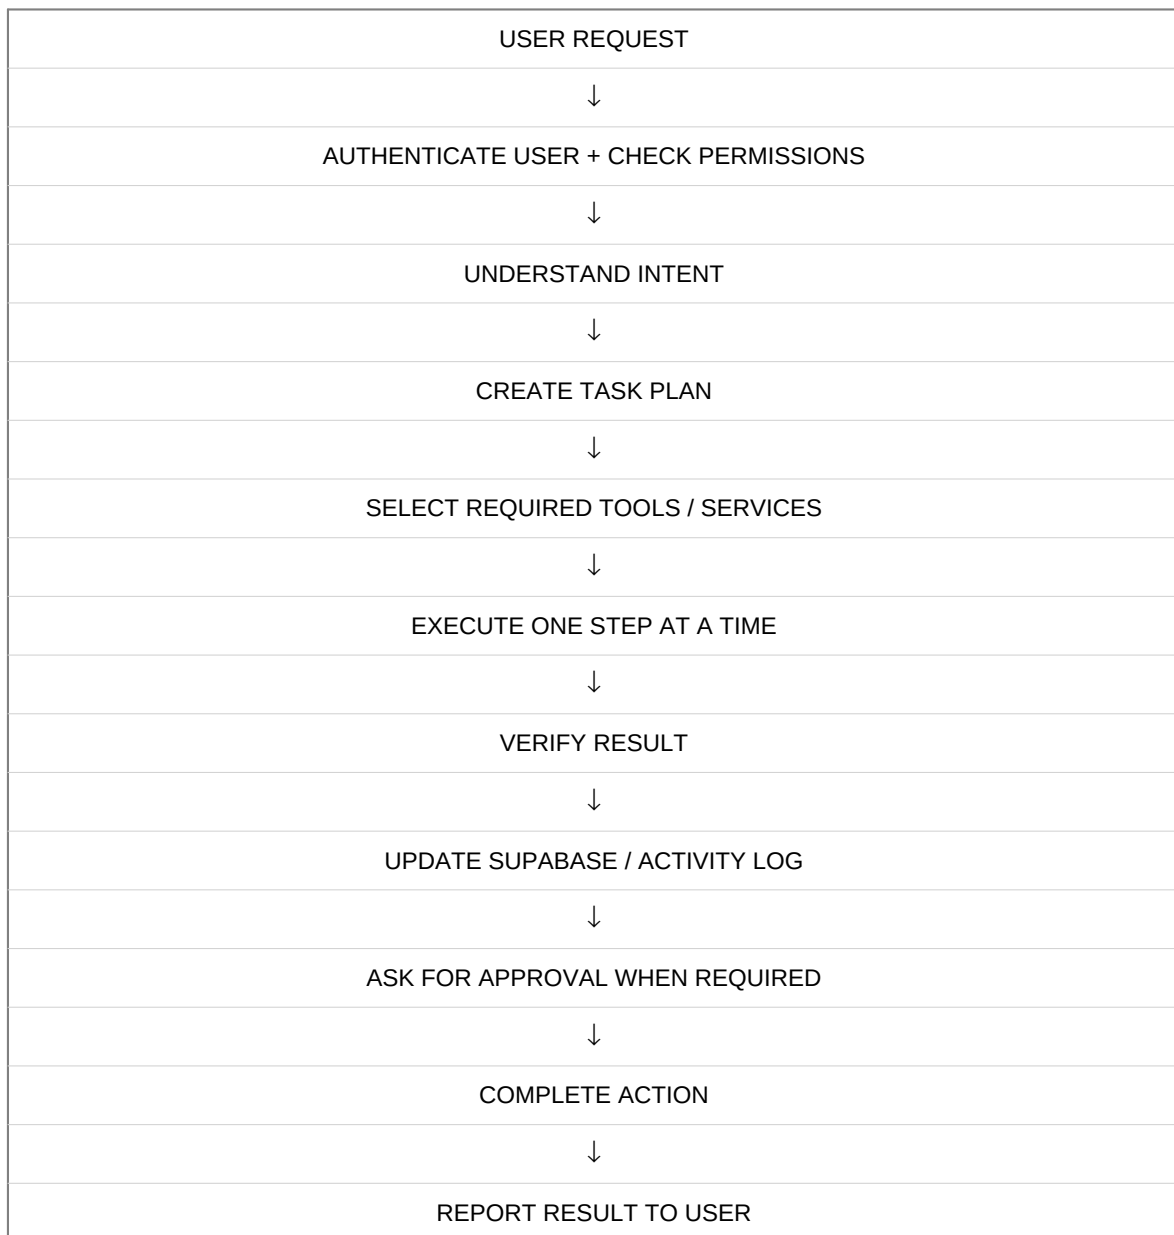

AI safety principle: irreversible, external or potentially high-impact actions should use explicit approval rules until the workflow is proven reliable.

9. Every Development Phase ka Standard Build Pattern



10. Development Phases — Detailed Build Order

Phase 0 — Foundation

- Finalize PRD, architecture, MVP scope, API capability verification, database plan, security rules, GitHub, Supabase and Vercel projects.
- Definition of Done: approved documentation + working repositories/projects + environment strategy.

Phase 1 — Project Setup

- Build Next.js/TypeScript foundation, backend/API structure, Supabase connection, authentication foundation, protected routes, error handling and logging.
- Definition of Done: user can securely reach a protected dashboard.

Phase 2 — Dashboard

- Build responsive navigation, overview, Social, Inbox, Content, Email, Clients, AI Assistant and Settings shells.
- Definition of Done: all primary routes exist with loading, empty and error states.

Phase 3 — Social Connections

- Implement common integration interface and platform adapters. Implement OAuth/token lifecycle and account status.
- Definition of Done: a supported platform can be connected, stored securely, refreshed where supported and disconnected.

Phase 4 — Content

- Upload, validate, store and manage media. Create content records and drafts.
- Definition of Done: user can upload media and manage it from Content Library.

Phase 5 — Publishing

- Add platform-specific publishing, scheduling, status tracking, retries and failure visibility.
- Definition of Done: supported content can be published/scheduled and result is visible.

Phase 6 — Unified Inbox

- Ingest supported messages/comments/mentions, normalize records, build conversation UI and filters.
- Definition of Done: supported communication appears in one inbox with platform identity and thread history.

Phase 7 — AI Communication

- Classify messages, generate replies, preserve conversation context and enforce approval workflow.
- Definition of Done: AI can generate useful suggestions and approved replies are sent through supported APIs.

Phase 8 — Client CRM

- Client profile, notes, communication history, social links, email activity and status lifecycle.
- Definition of Done: client information is centrally accessible and linked to relevant activity.

Phase 9 — Email System

- Templates, client selection, personalization, preview, sending and delivery/activity logging.
- Definition of Done: approved email can be sent through configured provider and logged.

Phase 10 — Email Automation

- Rules, delays, follow-ups, stop conditions, bounce handling and sequence history.
- Definition of Done: sequence can run safely and stop when conditions require.

Phase 11 — Analytics

- Aggregate supported platform and email metrics with clear source/platform labels.
- Definition of Done: dashboard displays reliable available metrics without inventing missing data.

Phase 12 — AI Copilot

- Central task planner that coordinates content, social, inbox, CRM and email tools.
- Definition of Done: multi-step tasks execute with permissions, approvals and result reporting.

Phase 13 — Security & QA

- RLS, authorization, secret handling, input validation, rate limits, webhook verification, duplicate protection and full regression tests.
- Definition of Done: release checklist passes.

Phase 14 — Beta

- Internal Nibrexo use, real workflows, issue tracking, performance monitoring and documentation updates.
- Definition of Done: critical issues resolved and release candidate approved.

Phase 15 — Production

- Production deployment, custom domain, monitoring, backups/recovery plan and operational documentation.
- Definition of Done: production system is live and maintainable.

11. GitHub & Version Control Rules

- main = production-ready code.
- development = integration branch.
- feature/* = individual development tasks.
- One logical change per commit where practical.
- No secrets, API keys or production credentials in Git.
- Pull request required before protected branch merge.
- Tag stable milestones, for example v0.1.0-mvp-foundation.
- Keep documentation updated with architectural changes.

12. MVP Scope

- Authentication and protected dashboard
- Supabase database + storage
- Social account connections
- Content library
- Supported multi-platform publishing
- Unified inbox foundation

- AI reply suggestions
- Client CRM
- Email templates + provider sending
- Basic email automation
- Testing and security baseline

13. Post-MVP

- Advanced AI Copilot
- Advanced scheduling
- Analytics
- Team collaboration
- Client workspaces
- Billing / SaaS plans
- Additional integrations
- More autonomous workflows

Document Version: 1.1 | Product: Nibrexo OS AI | Owner: Nibrexo
